



TAHOE TRUCKEE

UNIFIED SCHOOL DISTRICT

Measure U
Safe and Modern Classrooms
21st Century Learning

May 1, 2018



Measure U – Project Schedule

2016 Completed Projects:

- Alder Creek Middle School: Parking Lot Upgrade/Security/21st Century Learning
- Glenshire Elementary School – Phase 2: Modernization/Security/21st Century Learning
- Sierra Expeditionary Learning School: Parking Lot Upgrade/Modernization/21st Century Learning
- Donner Trail Elementary School: Exterior Painting/Gym Interior Painting/Gym Flooring
- Maintenance/Warehouse Facility
- Truckee High School: Pool Building Conversion

2017 Projects:

- New Maintenance/Warehouse Facility – Completed
- Truckee High School – Phase 2-Increment 1: West Wing and Site Work
- Donner Trail Elementary School: New Construction/Modernization/21st Century Learning

2018 Projects:

- Truckee Elementary School: New Construction/Modernization/21st Century Learning
- Truckee High School - Phase 2-Increment 2: Administration, Library, Girls Locker Room Upgrade and Modernization of Existing Building

Truckee High School



Phase I: Track/Parking/Restroom Complete

Phase II: New Construction/Modernization

Increment 1: March 2017 through August 2018

West Wing

Site Work

Increment 2: August 2018 through December 2019

Library

Administration


Girls Locker Room Renovation

Modernization of Existing Building



Truckee High School

Truckee High School Site Access Plan for 2017-2018 School Year

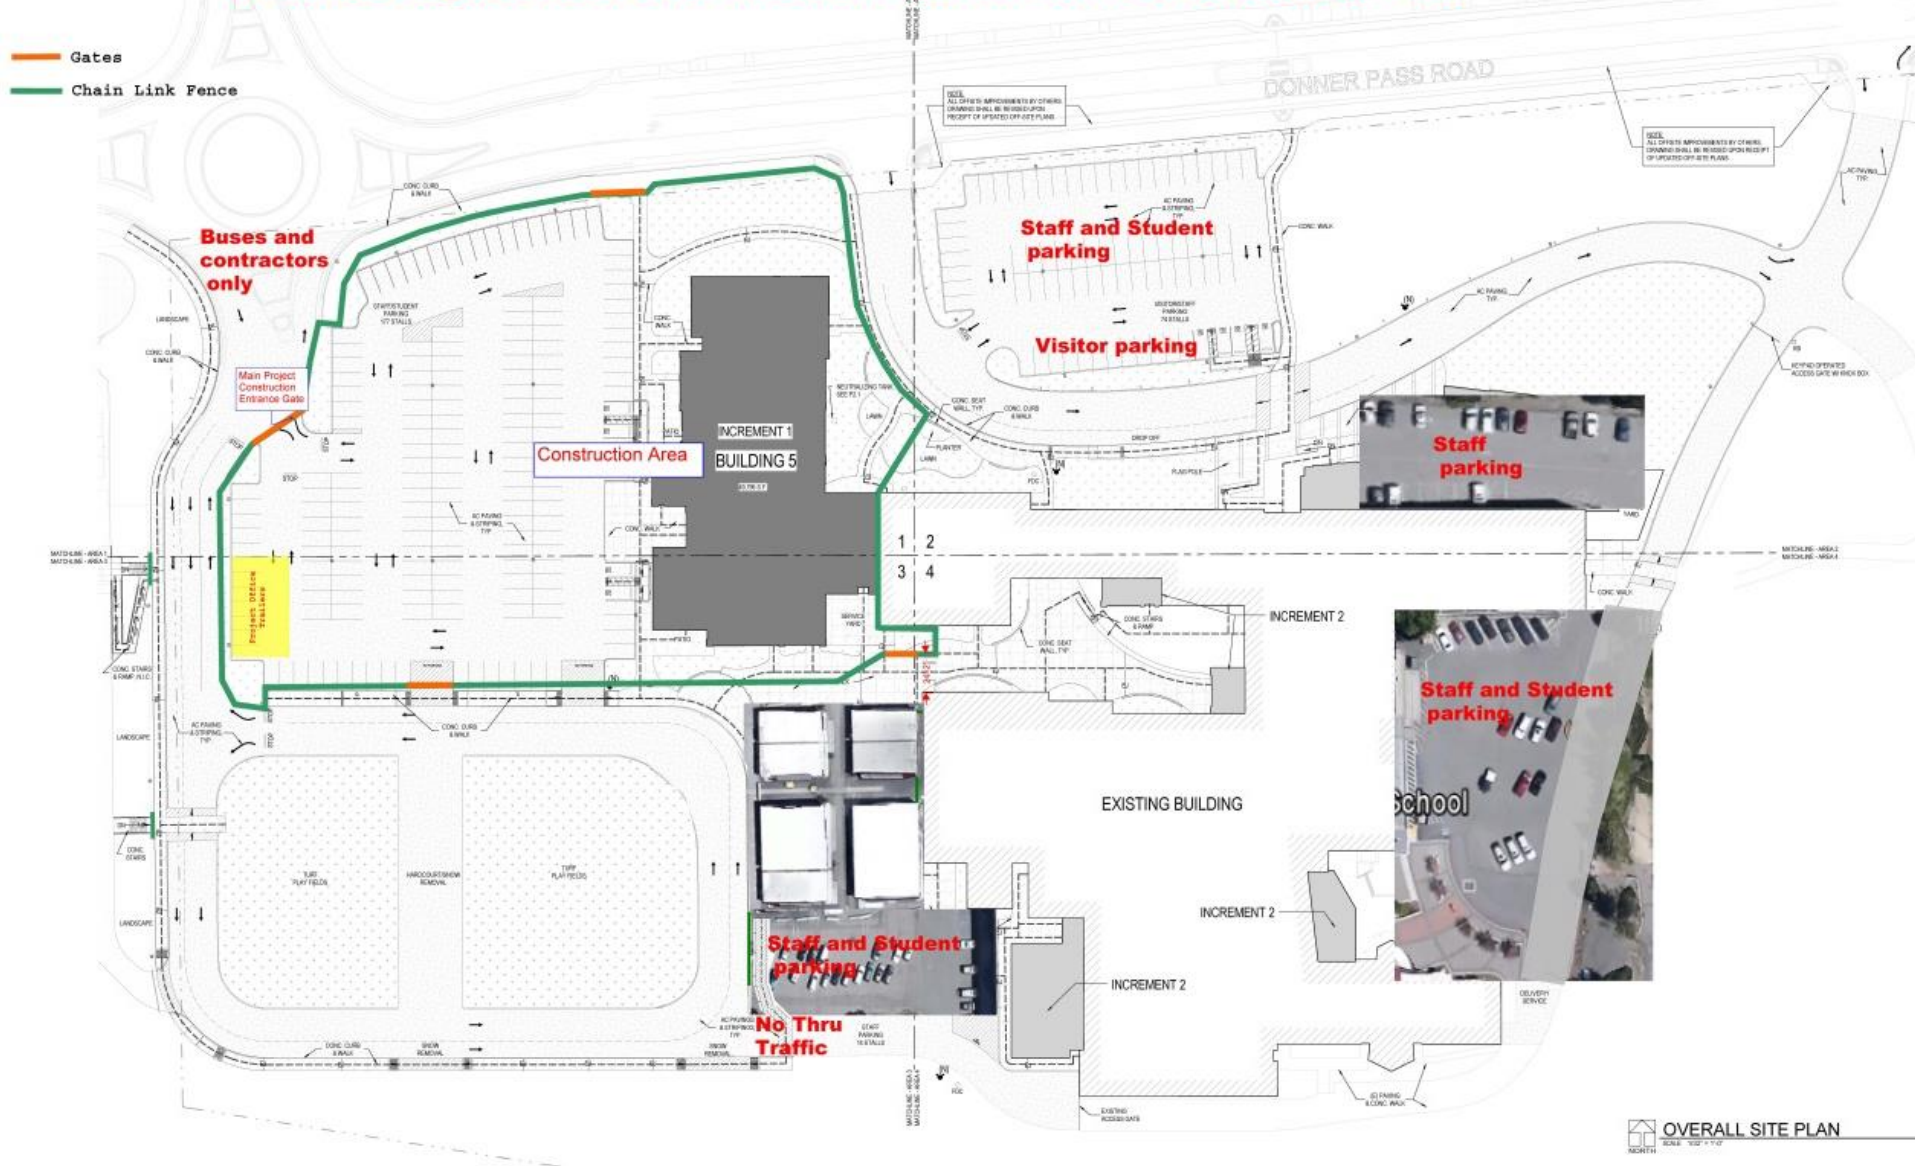

Truckee High School



Truckee High School



Truckee High School




Truckee High School



First Floor Plan

Increment 2

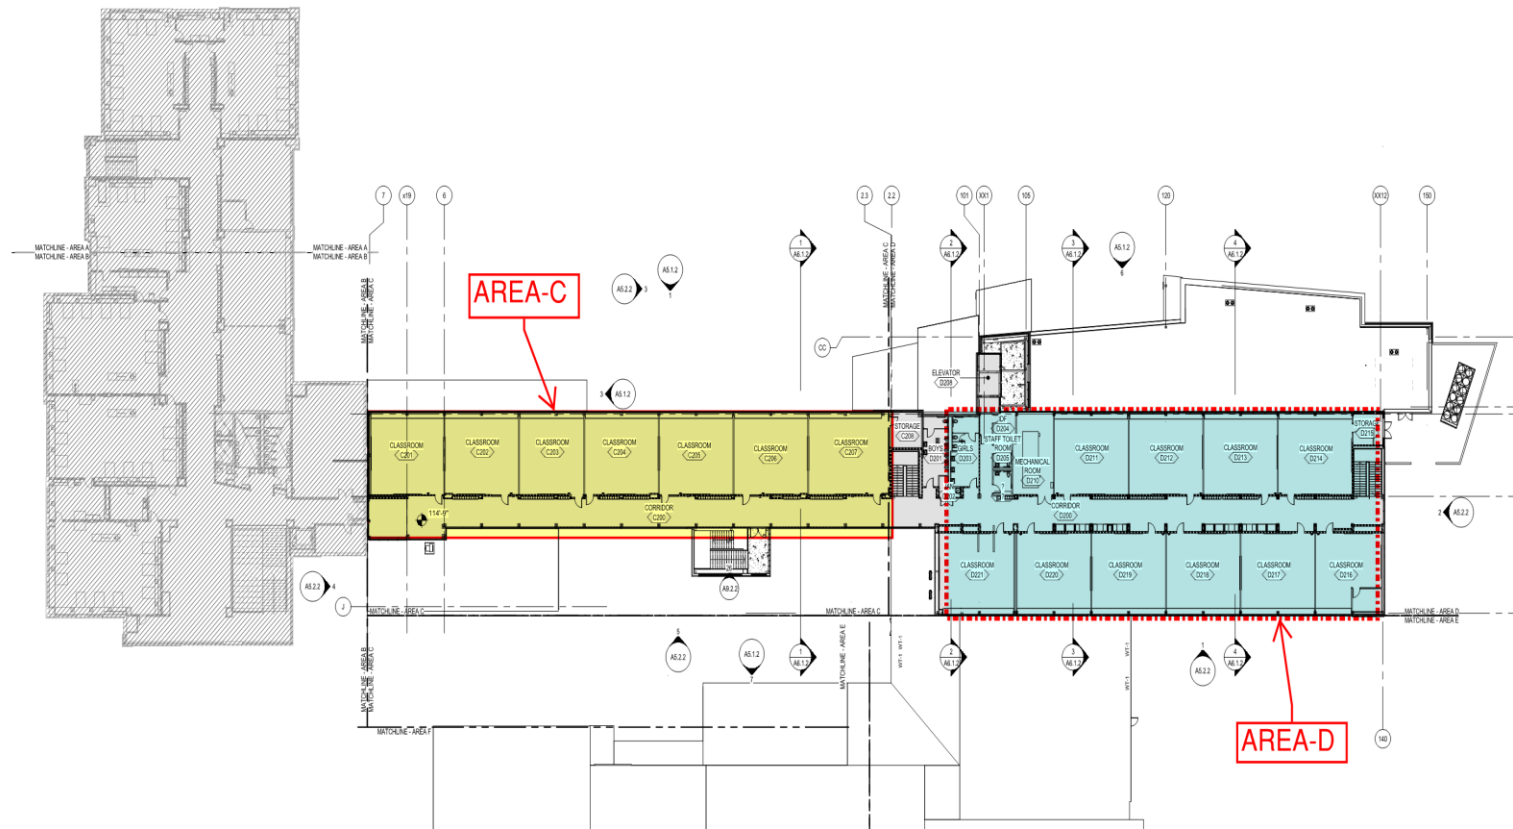

First Floor Plan

Increment 2



Truckee Elementary School



Project Schedule

- Submitted to DSA in May 2017
- Bid Project February 2018
- Start Construction in April 2018
- Construction Completed by Fall 2020

Project Architect: DLR Group

TTUSD Project Manager: Anna Klovstad

Contractor: Sundt Construction

Site Budget: \$34,614,849


TRUCKEE ELEMENTARY SCHOOL

Truckee Elementary School



Truckee Elementary School

PHASING PLAN DATED SEPTEMBER 2017

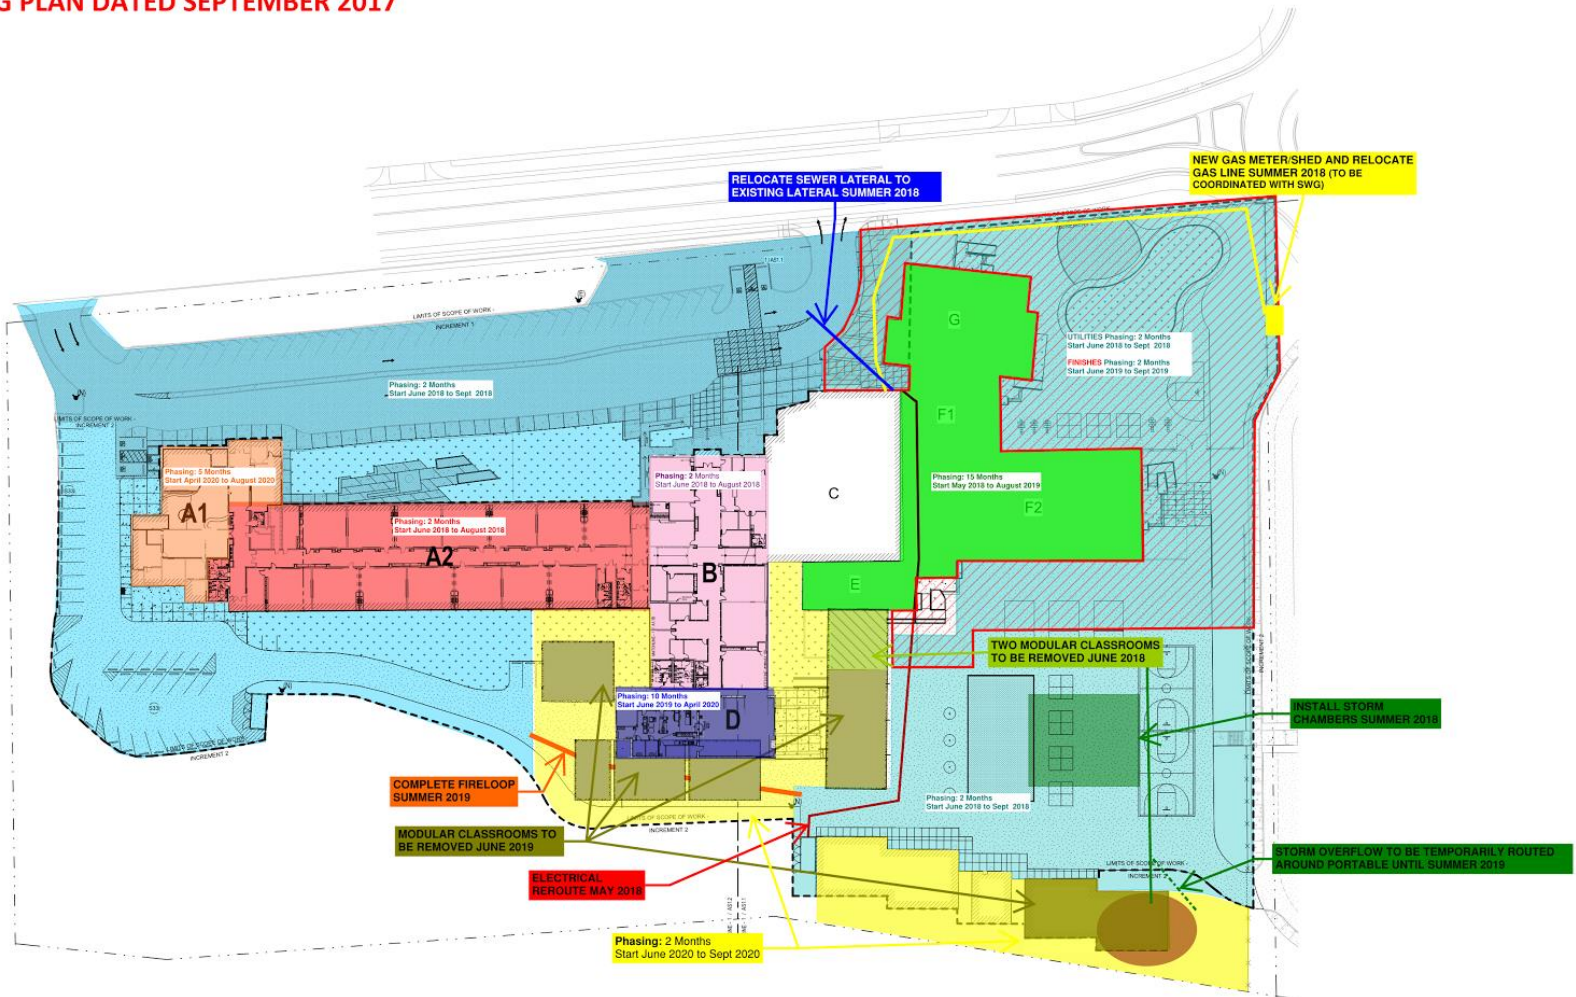

Donner Trail Elementary School



Project Schedule

- Submitted to DSA on September 29, 2016
- Project Bid Twice
- Start Construction in June 2017
- Construction Completed by May 2018

Project Architect: JK Architecture Partnership

TTUSD Project Manager: Will Broad

Contractor: Reyman Brothers

Contractor Bid: \$3,770,000

Site Budget: \$4,942,342




Donner Trail Elementary School



Donner Trail Elementary School



Donner Trail Elementary School

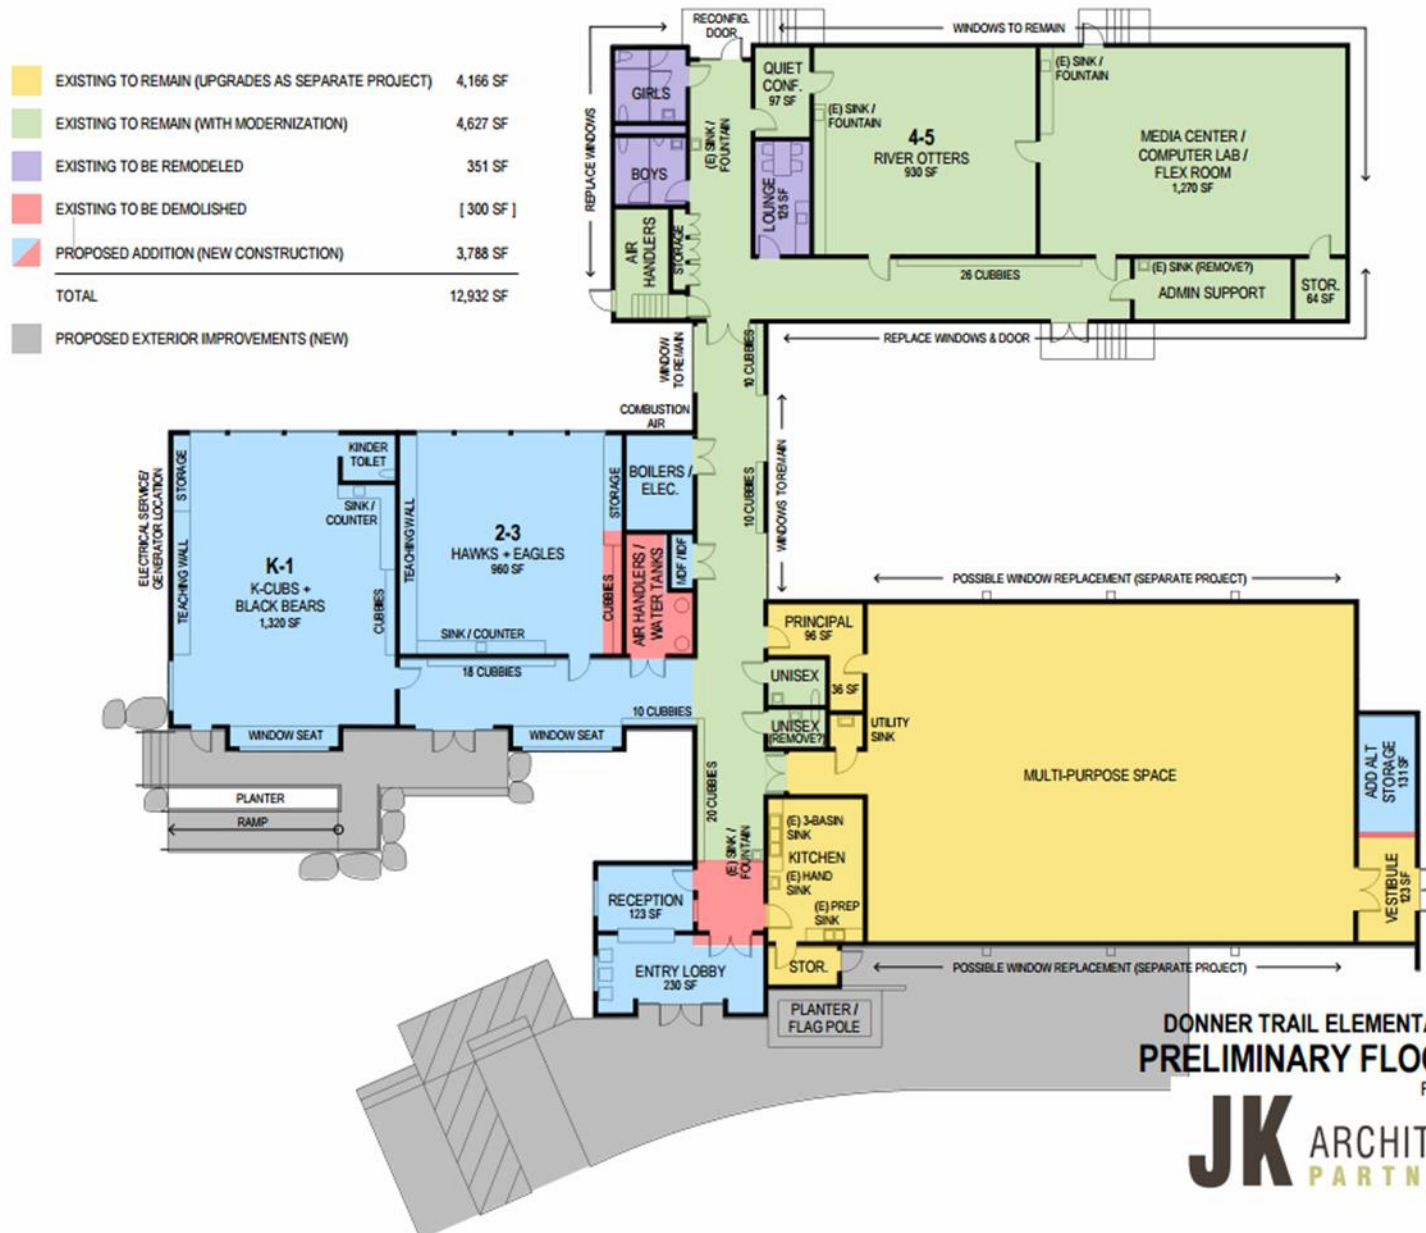

QUESTIONS

