


TRUCKEE HIGH SCHOOL

FACILITY UPGRADE PROJECT






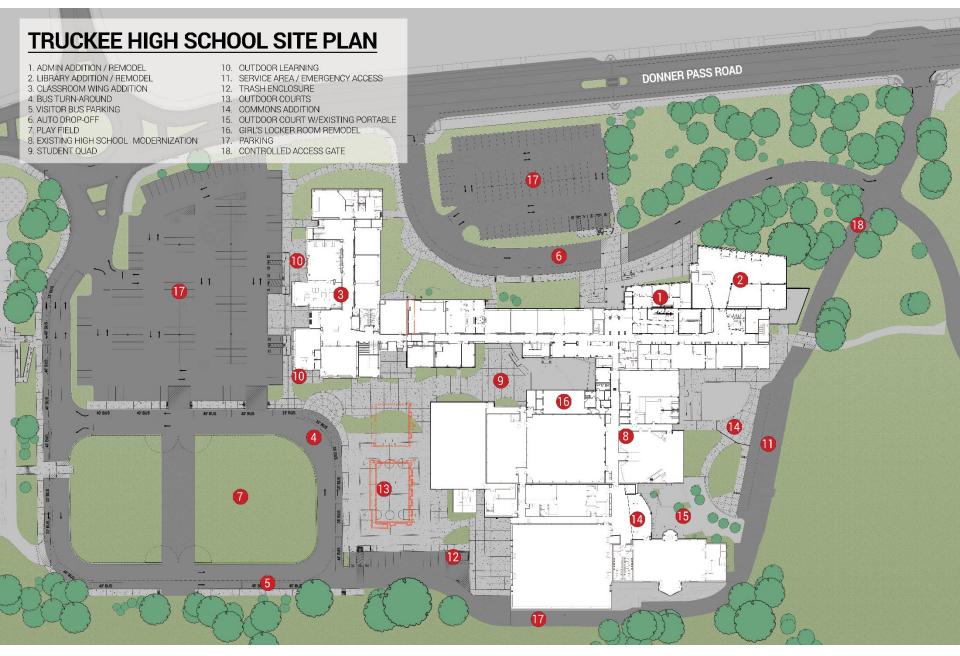




First Floor Plan

PHASE 1

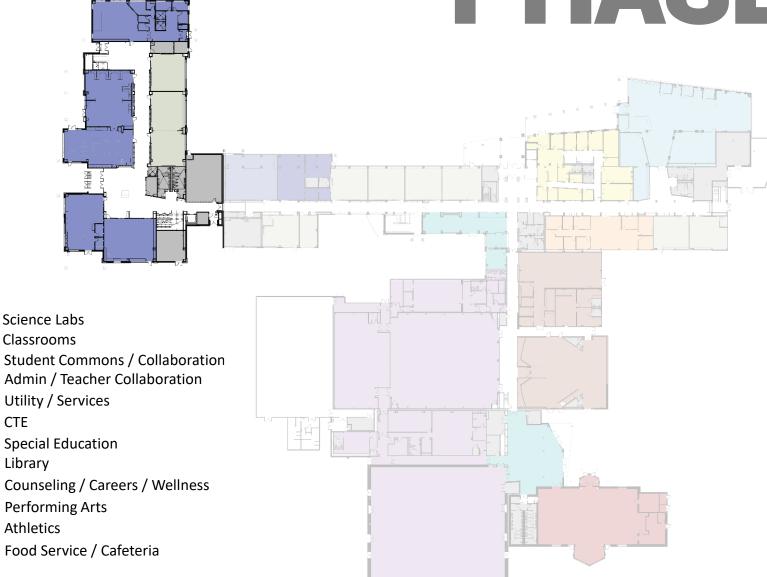






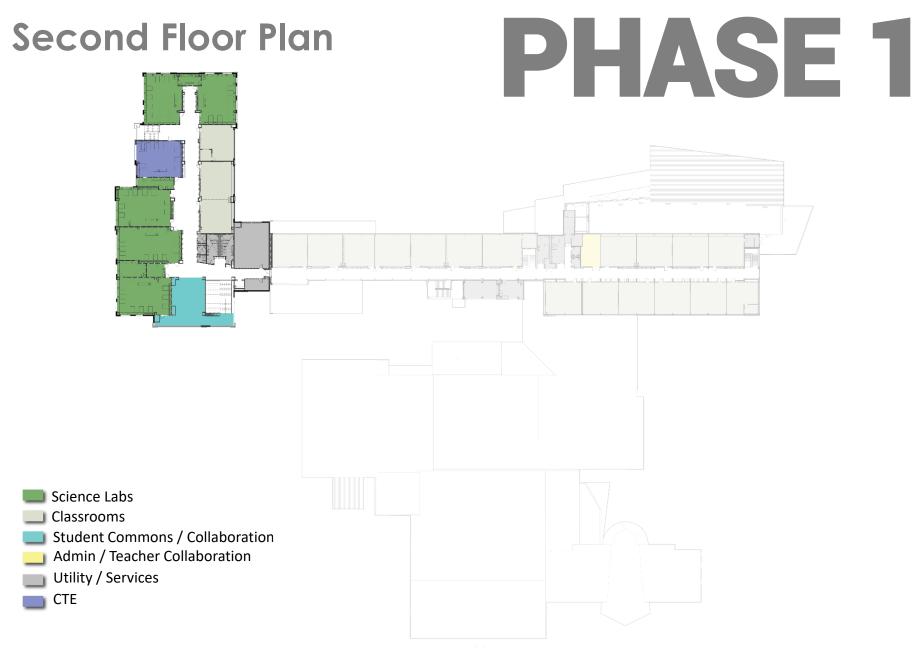





Temporary / Emergency Exit PHASE 1

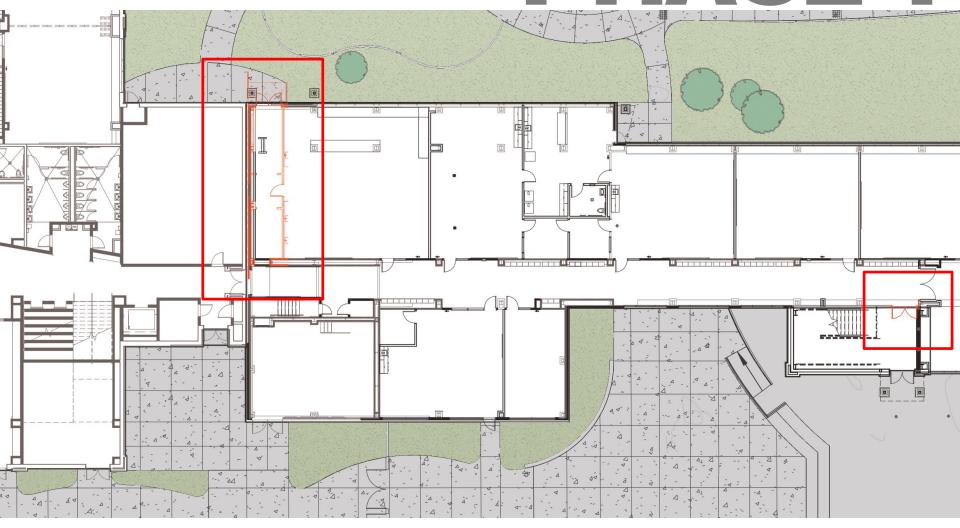





New West Wing-First Floor Plan







New West Wing - Second Floor Plan








First Floor Plan


PHASE 2

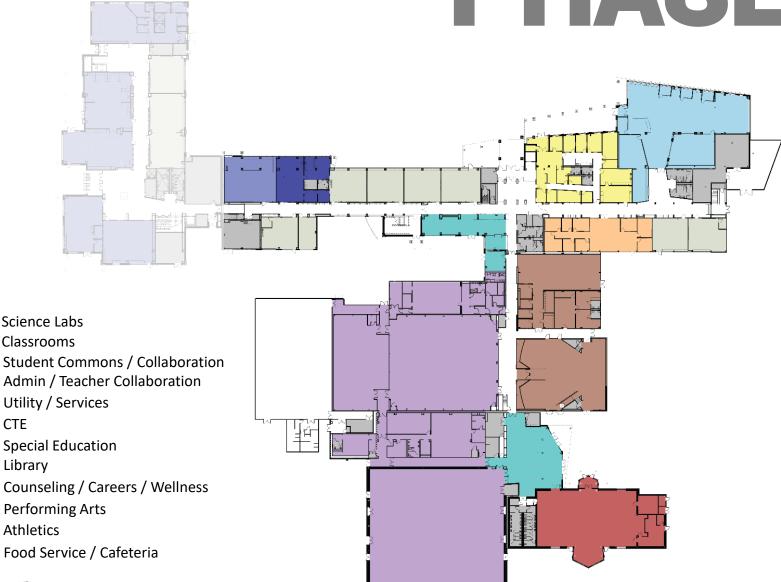



Truckee High School Modernization

LR Group

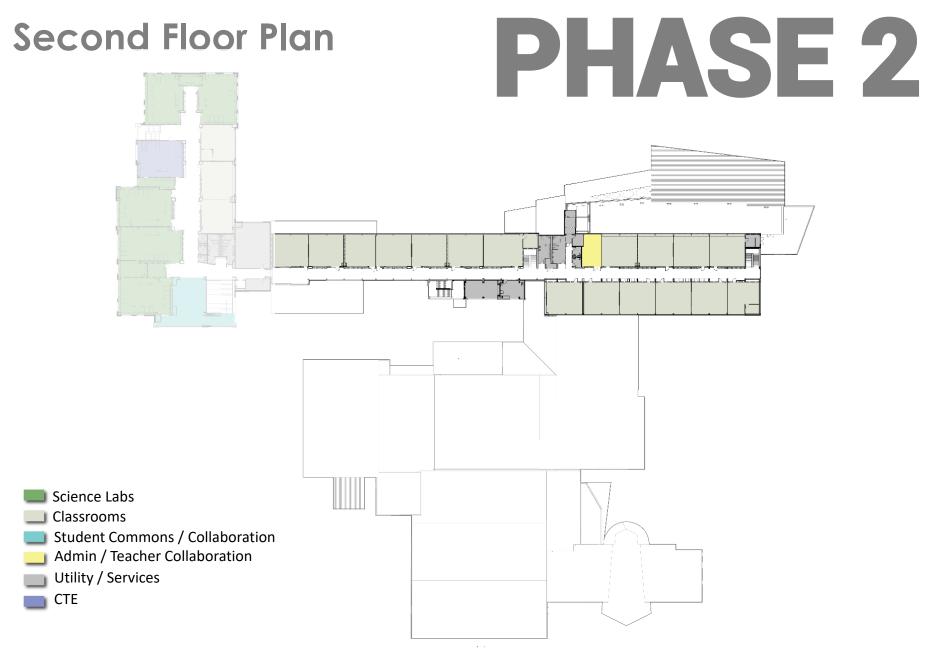






CONSTRUCTION





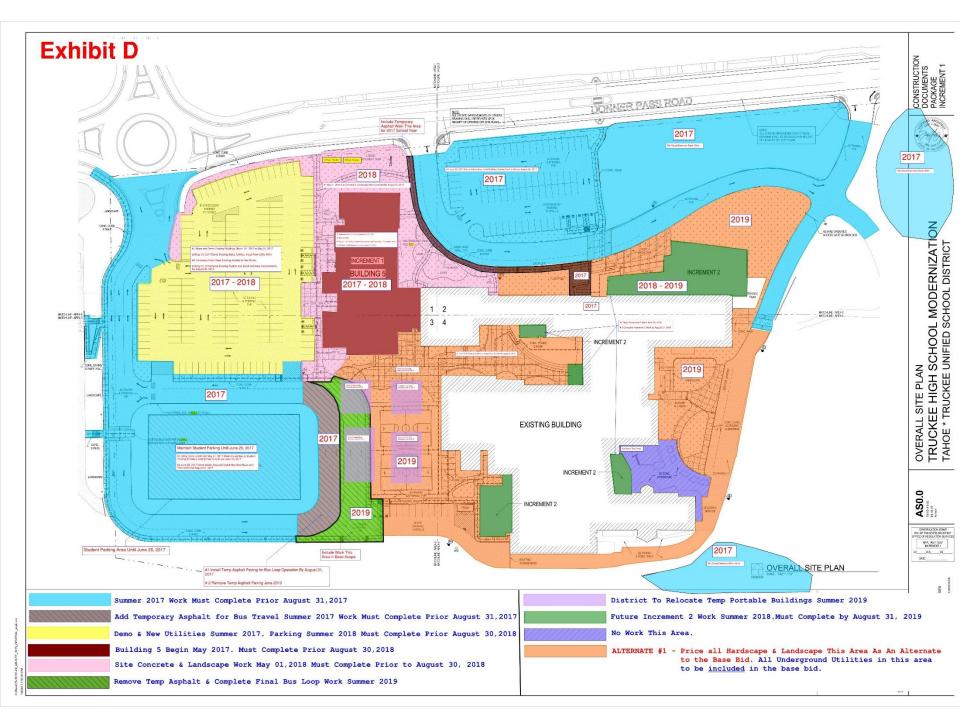



10																																														
			2017						2018							2019									2020																					
O N D	J F	М	A I	M J	J	Α	S	0	N	D	J	F	M	Α	M	J	J	Α	S	0	N	D	J	F	М	Α	М	J	J	Α	S	0	N	D	J	F	M	A	М	J	J	Α	S	0	N	D
20																																														

ACTIVITIES:

Elementary School:


No Activities

- · Finish Pool House Renovation
- Relocate Ch. 6
- · Establish Temporary Construction trailer at old IT building
- Abatement of out-buildings









ACTIVITIES:

Elementary School:

No Activities

- · Demolition of out-buildings
- Establish new student egress from central wing, 4/7/16 4/16/16
- Abate Ch. 6, wood shop and bus maintenance, 4/7/16 4/16/16







25										
		2017 2018 2019 2020	2020							
O N D J F M A	M	J A S O N D J F M A M J J A <mark>S O N D J F M A M J J A S O N D J F M A M J J A S O N D J F M A M J J A S O N D D D D D D D D D D D D D D D D D D</mark>	D							

ACTIVITIES:

Elementary School:

No Activities

- Complete Building Demolition, Slab and Footings
- · Begin Site Demolition, Utility and Foundation work







		2017		2018	2019	2020							
O N D	J F M A M	J ,	S O N D	J F M A M J J A S O N D	J F M A M J J A S O N D	J F M A M J J A S O N D							

ACTIVITIES:

Elementary School:

• Establish Temporary Location for Elementary School Apparatus

- Mobilize Construction Office and Establish Yard
- · Begin West Expansion
- · Begin and Complete Sitework as Indicated







F M A M J J S O N D J F M M J J A F M A M J J A S O N D

ACTIVITIES:

Elementary School:

No Additional Activities

· Continue west expansion

High School:

· Begin and Complete girls locker room







ACTIVITIES:

Elementary School:

· No Activities

- Continue west expansion
- Begin library expansion (PM Shift)







	2017		2018		2019	2020
O N D	J F M A M J J A S O N D	J F M A M	J A	S O N D	J F M A M J J A S O N D	J F M A M J J A S O N D
80			To the second se			

ACTIVITIES:

Elementary School:

- · Begin Elementary School East Wing, sitework and utilities
- · Start / Finish Classroom Modernization / North Parking

- Complete West Expansion
- Modernize L2 Classrooms
- Complete West Parking
- Continue Library Expansion
- · New Quad Stair Tower
- · Demo Locker Room









McGregor Lake Ledge, squares & recs







STONE








WOODTONE - Rustic Series Old Cherry






WOOD



















EXTERIOR RENDERING







EXTERIOR RENDERING







EXTERIOR RENDERING








INTERIOR FINISHES





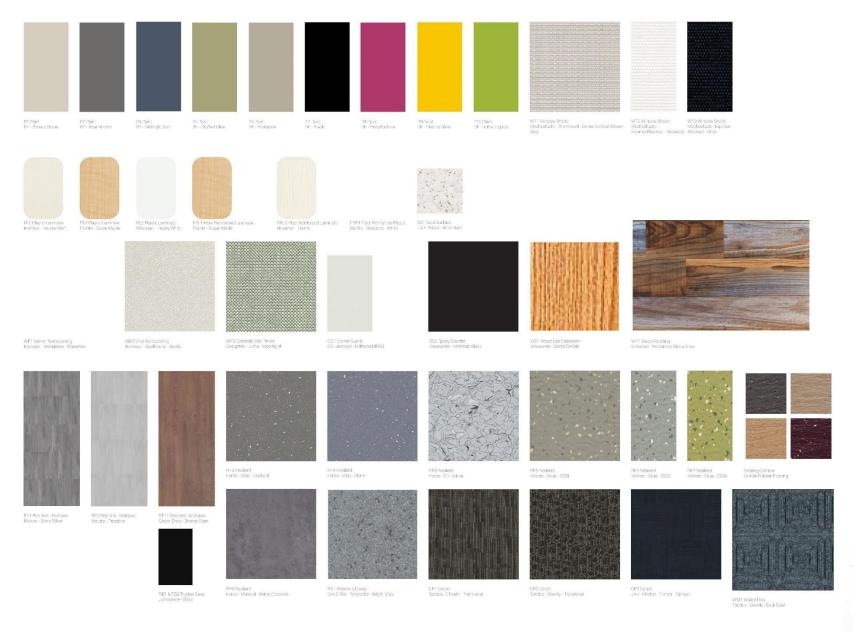



Tahoe Truckee Unified School District Truckee High School Modernization DLB Group Project Number 75-15110-00

FLOOR FINISHES

New West Wing-First Floor Plan










FLOOR FINISHES New West Wing-Second Floor Plan





ART ROOM

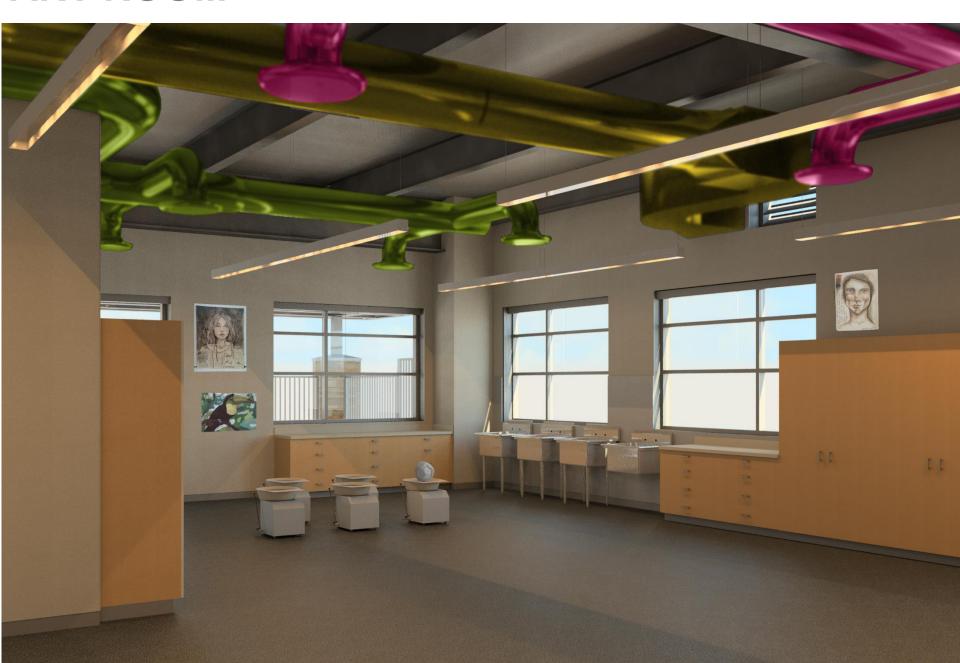

GRAND STAIR – STUDENT COMMONS







CLASSROOM





THANK YOU!
