



Measure U
Safe and Modern Classrooms
21st Century Learning

October 9, 2018

Measure U – Project Schedule

2017 Projects:

- New Maintenance/Warehouse Facility: Completed
- Truckee High School: Increment 1 West Wing and Site Work Completed
- Donner Trail Elementary School: New Construction/Modernization/21st Century Learning - Completed

2018 Projects:

• Truckee Elementary School: New Construction/Modernization/21st Century Learning

2019 Projects:

- Truckee Elementary School: New Construction/Modernization/21st Century Learning
- Truckee High School: Increment 2 Administration, Library, Girls Locker Room Upgrade and Modernization of Existing Building

Truckee High School



Phase I: Track/Parking/Restroom Complete

Phase II: New Construction/Modernization Increment 1: March 2017 through August 2018

West Wing Site Work

Increment 2: Jan. 2019 through Dec. 2019

Library
Administration
Girls Locker Room Renovation
Modernization of Existing Building



Truckee High School




Truckee High School





First Floor Plan

Increment 2

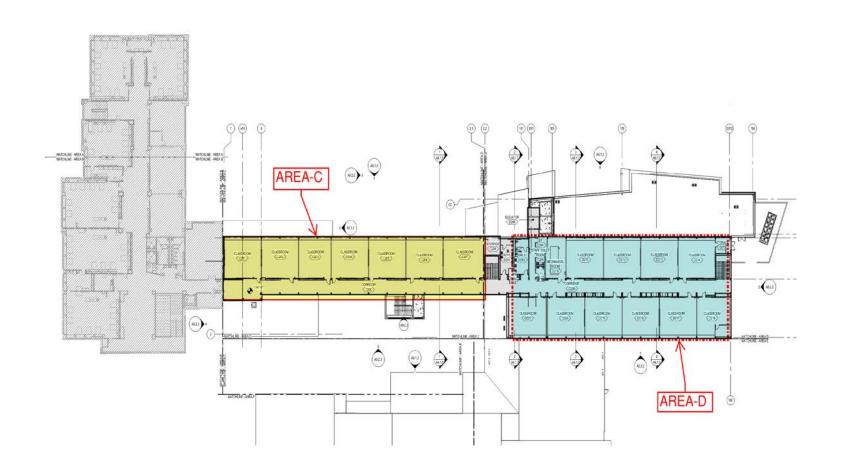

Truckee Elementary School



Project Schedule

- Submitted to DSA in May 2017
- Bid Project February 2018
- Start Construction in April 2018
- Construction Completed by Fall 2020

Project Architect: DLR Group

TTUSD Project Manager: Anna Klovstad

Contractor: Sundt Construction

Site Budget: \$34,614,849



TRUCKEE ELEMENTARY SCHOOL




MAIN ENTRY

Truckee Elementary School



Truckee Elementary School

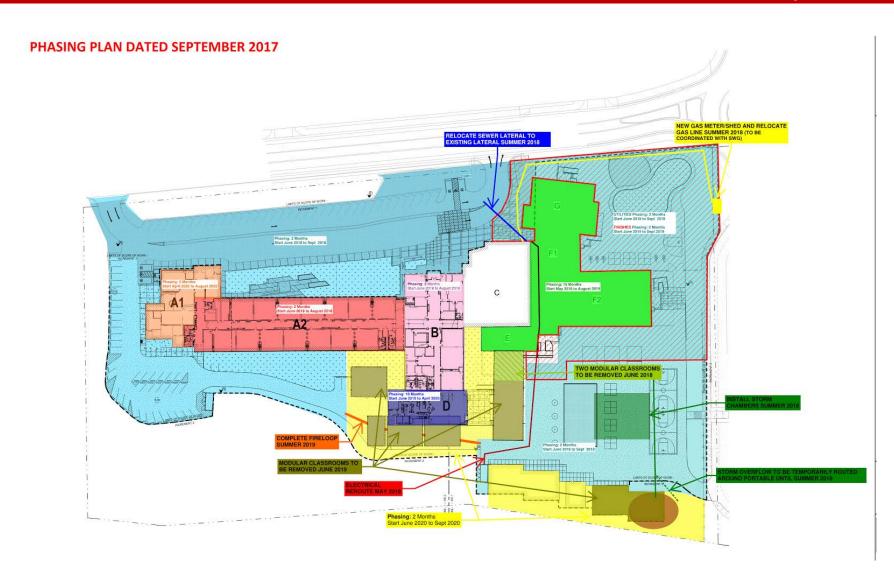

Donner Trail Elementary School



Project Schedule

- Submitted to DSA on September 29, 2016
- Project Bid Twice
- Start Construction in June 2017
- Construction Completed by August 2018

Project Architect: JK Architecture Partnership

TTUSD Project Manager: Anna Klovstad

Contractor: Reyman Brothers Contractor Bid: \$3,770,000 Site Budget: \$4,942,342

Donner Trail Elementary School



Donner Trail Elementary School



